
S.O.D Building Report

Kahindo Cecile • 07.19.2024

Overview

Building Construction Status

The construction of the Orphans building is currently in progress

Recent progress: 1st Phase Completion

- First phase (Ground floor) of the project was completed (without tiles)
- **Cost:**
 - Foundation: USD \$17,745.50
 - Walls: USD \$24,911.54
 - **Total: USD \$42,657.04**

Next Phase: In Progress

We are currently building the first, second and third floor of the building

In Progress & Remaining amount

All Amounts In USD	Ground	1st Floor	2nd Floor	3rd Floor	Roof
Foundation	\$ 17,745.50	\$ -	\$ -	\$ -	\$ -
Walls	\$ 24,911.54	\$ 26,344.44	\$ 26,344.44	\$ 18,044.64	\$ -
Tiles	\$ -	\$ 42,607.50	\$ 40,911.00	\$ 44,246.25	\$ -
Masons	\$ 15,155.84	\$ 15,738.76	\$ 15,738.76	\$ 8,765.67	\$ -
Roofing	\$ -	\$ -	\$ -	\$ -	\$ 17,988.25
Total	\$ 57,812.88	\$ 84,690.70	\$ 82,994.20	\$ 71,056.56	\$ 17,988.25
TOTAL Budget	\$314,542.59				
Total Needed	\$271,885.55				

Note: The amount in green has already been raised and used on the ground floor. Thank you to everyone who contributed already.

Summary

Each section above may include one of the following but not limited to:


- Construction materials such as:
 - Cements, sand, timbers,
 - Nails
 - Blocks
 - etc...
 - Restauration of engineers and macons
 - Transportation
 - Labor for the principal engineer and macons
-

Schedule

Completion of Ground
Floor

Completion of 2nd
floor

Completion of roofing

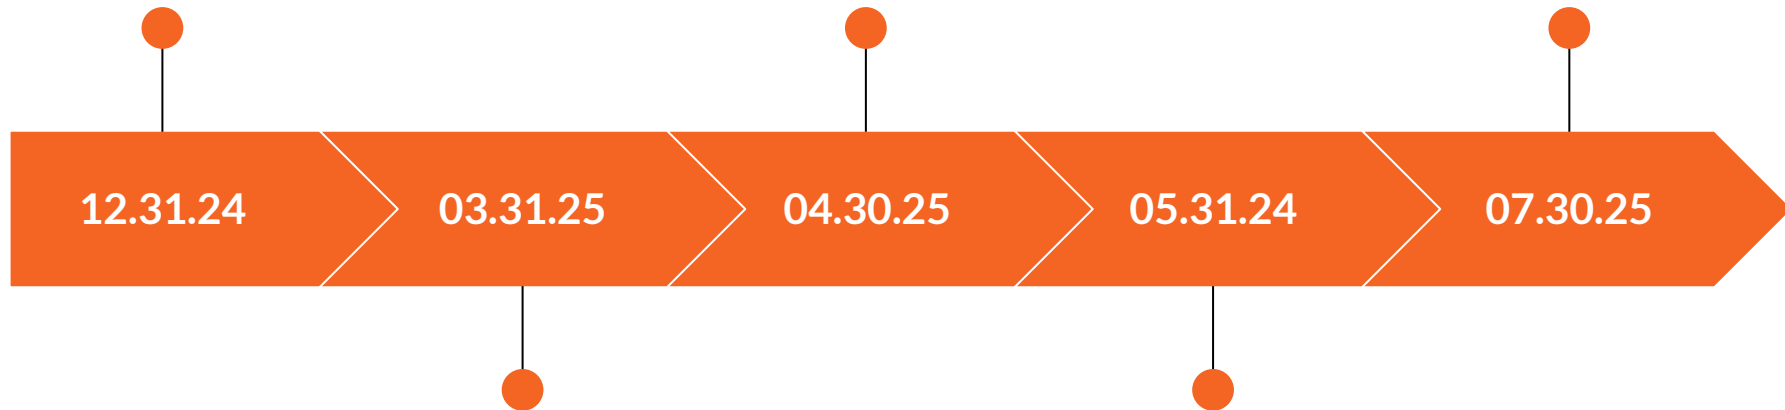

Completion of 1st floor

Completion of 3rd
floor

Next steps

Fundraising campaign

We are currently fundraising in order to fully complete the ground floor and the rest of the building

Building Inauguration

Once the building is completed, we will proceed with praying and inaugurating the house

Fundraise for furnitures and move in

Once the building is complete, we will fundraise to buy furnitures and move in the kids.

Thank you from
S.O.D.

